


## **Project Title: 0103 - Physical Infrastructure (Houses and Containers)**

**Name of Implementing Agency:** Department of Urban Development and Building Construction (DUDBC), Division Offices

**Contact Person:** Mr. Chatur Raj Prasai, Senior Divisional Engineer (SDE), Morang and other SDEs of the concerned Division offices of the DUDBC

**Status:** Completed

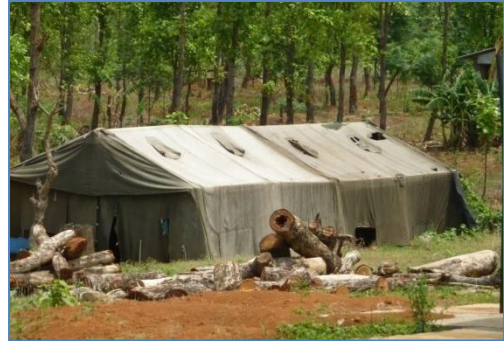

**Location:** 28 cantonment sites spread over different districts of the country

**Beneficiaries:** Maoists Combatants

### **Objectives:**

- To build health centres, common kitchens and toilets for the combatants, and the tent bases in the cantonment sites.

### **Summary of Achievements:**

- All of the physical targets constructed viz. 10 health centres (one additional was also built at Dudhauri due to local demand), and 31 platoon kitchens.
- A total of 118 platoon toilets were constructed against the target of 145 (81% achieved). Similarly, 79.5% progress was reported in building the tent bases – 798 bases were built against the target of 1004.

### **Outcomes:**

- Improved living conditions of combatants in the cantonments.
- Better hygienic environment due to use of toilets.

### **Issues:**

- Infrastructure facilities are not gender friendly. For example; toilets are shared for female and male combatants. Male and female combatants live in one shelter, often discomforting the female combatants.
- Inadequate number of toilets and existing toilets requiring maintenance.
- Some temporary shelters are worn out and need maintenance.
